



New Women and Babies Hospital Project

Fiona Stanley Hospital precinct

September 2025

The WA Government is building a world-class Women and Babies Hospital and expanding facilities at Osborne Park Hospital and Perth Children's Hospital.

The new hospital will be built on land within the Fiona Stanley Hospital precinct where two new multi-deck car parks will also be delivered as part of this project.

What's happening in September?

New Women and Babies Hospital

This month, the Managing Contractor continues work on sections of staff car parks 8 and 9 – the site for the new Women and Babies Hospital.

These works will include service location, removal of kerbing, light poles and asphalt. Surveying will also continue along Jennalup Street and Fiona Wood Road.

From 1 October, these car parks will fully close to hospital staff so the Managing Contractor can take full possession of the site.

New multi-deck car parks

To facilitate construction of the first multi-deck car park, preliminary investigation works are continuing to test ground conditions and identify underground utilities to inform the design of the car park. These investigations will continue until construction starts in late 2025.

Work crews will be mostly working within the site of the new car park, currently referred to as car park 3. However, at times there will be testing on adjacent paths and local roads (Jennalup Street and Winch Way).

As part of early planning for a proposed second multi-deck car park, geotechnical investigations will be undertaken within car park 7, near Fiona Wood Drive.

What to expect

- General construction noise and vibration during some activities.
- Construction vehicles and equipment including, but not limited to, heavy vehicles, survey equipment, compactor, hand tools (powered and non-powered).
- Mitigation measures will be in place to minimise impacts where feasible, including:
 - noise and vibration monitoring
 - water carts and hoses for dust suppression.




Changes to traffic, pedestrian and cyclist routes

Given the proximity of some works to local roads, there may be short-term impacts to traffic in the area. Traffic control and signage will be in place where required to safely assist construction staff, motorists, pedestrians, and cyclists. This may include redirecting traffic and stop-slow traffic controls.

Work areas

The image below shows the upcoming work areas:

- Car park 3 – preliminary investigation works are taking place ahead of construction of the first multi-deck car park.
- Car parks 8 and 9 – enabling works for the new Women and Babies Hospital continue during September, including service location, removal of kerbs, lights, and asphalt. Stage 2 site possession will see staff car parks 8 and 9 closed to hospital staff from 1 October.
- Car park 7 – early investigations commencing to support planning works for an additional proposed multi-deck car park.

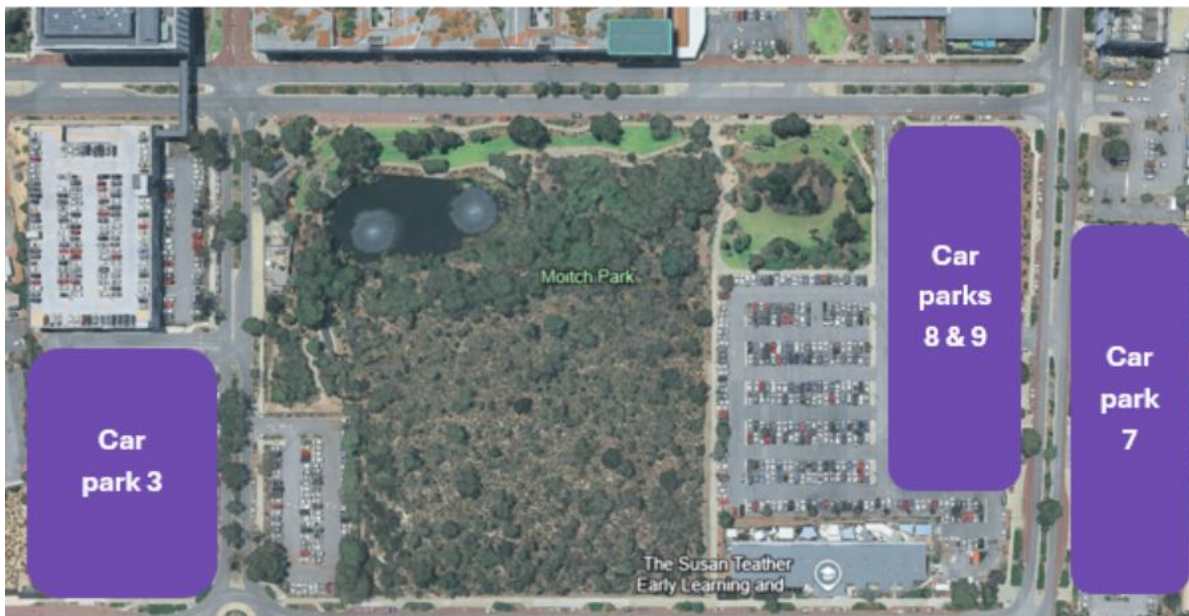

Feedback

For more information about the project please visit womenandbabieshospital.wa.gov.au or www.buildingfortomorrow.wa.gov.au/projects/new-women-and-babies-hospital-project.

If you would prefer to receive updates by email, please contact womenandbabies@omid.wa.gov.au and we will add you to the distribution list.

Thank you for your cooperation while we complete this essential work.
