



# New Women and Babies Hospital Project

## Construction update - Fiona Stanley Hospital precinct

June 2026

Construction is progressing on the new Women and Babies Hospital and first multi-deck car park, both located within the Fiona Stanley Hospital precinct in Murdoch.



*Aerial picture of Women and Babies Hospital site*

## What's happening on site?

### Women and Babies Hospital construction site

Over the coming months, installation of an additional five tower cranes is expected. The first three of eight cranes were delivered during May, including the largest tower crane on site which will facilitate the central core build.

With foundation works advancing and the slab for the lifts and stairwells now complete, construction of the main building structure is set to begin. This phase includes a concrete pour for the starter walls - essential for supporting a specialised vertical system that enables construction of the core structure, floor by floor, through to completion.



Last month, the project reached a major construction milestone with what is expected to be the largest single concrete pour on the project. This pour helped create a central foundation for the lifts and stairwells, supporting the heaviest part of the hospital building. More than 2,200 cubic metres of concrete was poured, involving 400 concrete delivery trucks and three mobile pumps, over 12-hours.

Upcoming works for the Women and Babies Hospital include:

- Completion of a new entry to site from Jennalup Street.
- Concrete pours to construct the remaining tower crane footings.
- Continuation of sheet piling to support excavation to build the site access track for vehicles exiting site.

### Multi-deck car park construction site

Work is progressing on the foundations for a new multi-deck car park being constructed as part of the New Women and Babies Hospital Project.

Concrete pours for the final raft footing for the stair and lift cores have been successfully completed, along with the first concrete pour for the ground slab.

Installation of inground services for the building has also commenced, and wall and column construction is advancing across the site.



*Aerial picture of the new car park site*



## Within the precinct

### Road modifications to support increased traffic

From mid-to-late June 2026, Jennalup Street will be modified to create additional space to support construction activities taking place on the new multi-deck car park site.

These traffic arrangements are expected to remain in place until mid-2027.




Modified traffic arrangements at Jennalup Street from mid-to late June



## New entry and exits at hospital construction site

A new entry into the Women and Babies Hospital site off Jennalup Street will support an increase in deliveries.

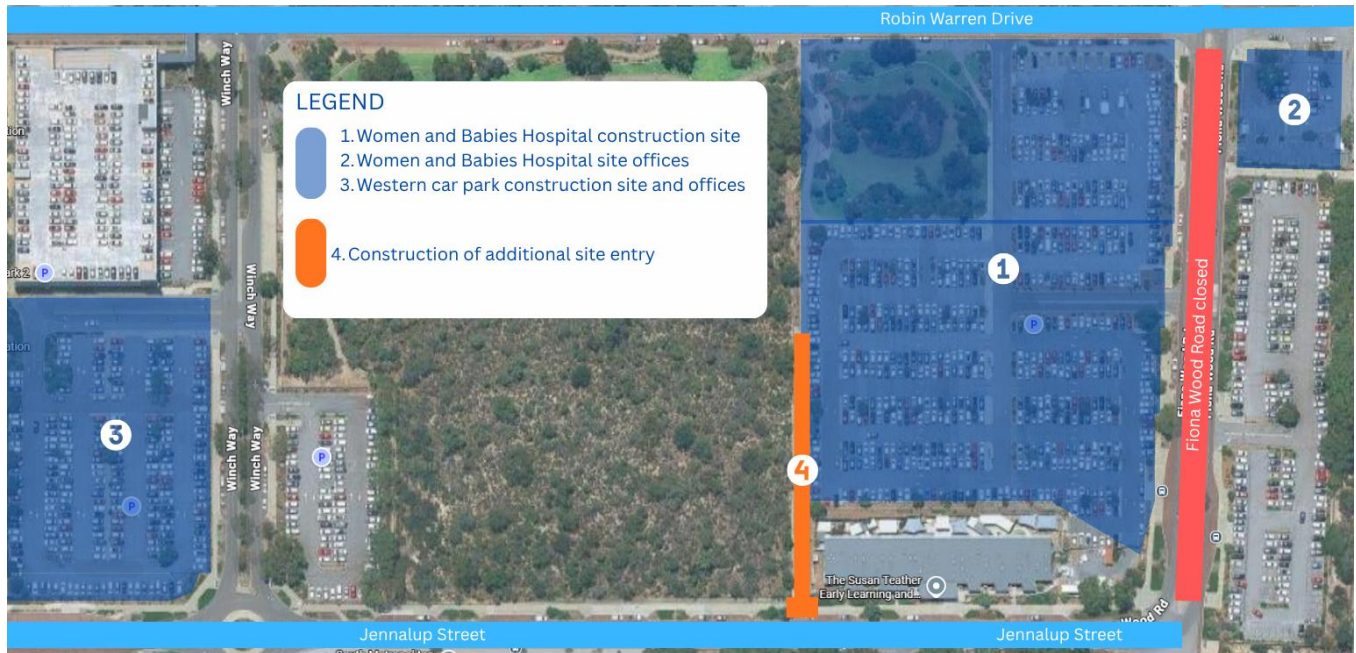

*Additional site entry at Jennalup Street*

## Working outside of normal hours

Out-of-hours works will continue throughout June.

Neighbouring businesses, residents and precinct users can expect some noise and lighting at both construction sites as well as increased traffic.

## Bus stop relocation

Bus stop #26983 at Jennalup Street (before Murdoch Drive) will relocate to opposite the Murdoch campus of South Metropolitan TAFE from mid-June 2026. Refer to Transperth for updates and timetables.

## What to expect from upcoming works

- General construction noise and vibration, particularly during sheet piling. Levels are continuously monitored to remain within safe, industry-approved limits.
- Increased traffic and heavy vehicle movements in areas where site works are taking place.
- Traffic management measures using signage and personnel to assist pedestrians, motorists and cyclists. This may include stop-slow traffic controls and temporary diversions.
- Construction vehicles and equipment, such as survey equipment, compactors and hand tools (powered and unpowered).



BUILDING  
FOR  
TOMORROW.



NEW  
WOMEN  
& BABIES  
HOSPITAL PROJECT



## Feedback and information

The landmark New Women and Babies Hospital Project will expand services and choice for women, newborns and families, replacing the century-old King Edward Memorial Hospital.

The 12-storey, 274-bed new Women and Babies Hospital includes inpatient facilities for gynaecology and maternity patients, a neonatology unit for newborns needing specialised care, operating theatres, a family birth centre and outpatient clinics. The project also includes a major expansion of Osborne Park Hospital.

For more information about the project please [visit the project page](#) or e-mail [womenandbabies@omid.wa.gov.au](mailto:womenandbabies@omid.wa.gov.au).

For questions specific to the multi-deck car park, please contact the Main Roads Customer Information Centre on 138 138 or email [enquiries@mainroads.wa.gov.au](mailto:enquiries@mainroads.wa.gov.au) referencing the Fiona Stanley Hospital Precinct Car Park Project.
